

May 2022 Readiness Working Group #5

Wednesday, 23 March 2022

This meeting is recorded for the purpose of
minute taking.

Please disconnect from your workplace VPN
for the Teams call



AEMO Competition Law Meeting Protocol

AEMO is committed to complying with all applicable laws, including the Competition and Consumer Act 2010 (CCA). In any dealings with AEMO regarding proposed reforms or other initiatives, all participants agree to adhere to the CCA at all times and to comply with this Protocol. Participants must arrange for their representatives to be briefed on competition law risks and obligations.

Participants in AEMO discussions **must**:

1. Ensure that discussions are limited to the matters contemplated by the agenda for the discussion
2. Make independent and unilateral decisions about their commercial positions and approach in relation to the matters under discussion with AEMO
3. Immediately and clearly raise an objection with AEMO or the Chair of the meeting if a matter is discussed that the participant is concerned may give rise to competition law risks or a breach of this Protocol

Participants in AEMO meetings **must not** discuss or agree on the following topics:

1. Which customers they will supply or market to
2. The price or other terms at which Participants will supply
3. Bids or tenders, including the nature of a bid that a Participant intends to make or whether the Participant will participate in the bid
4. Which suppliers Participants will acquire from (or the price or other terms on which they acquire goods or services)
5. Refusing to supply a person or company access to any products, services or inputs they require

Under no circumstances must Participants share Competitively Sensitive Information. Competitively Sensitive Information means confidential information relating to a Participant which if disclosed to a competitor could affect its current or future commercial strategies, such as pricing information, customer terms and conditions, supply terms and conditions, sales, marketing or procurement strategies, product development, margins, costs, capacity or production planning.

Agenda

Greg Minney



Agenda

#	Time	Topic	Presenter
1	10:00 – 10:05	Welcome and Agenda	Greg Minney
2	10:05 – 10:10	Actions	Greg Minney
3	10:10 - 10:20	May Program Update (include readiness for 21 March milestone review)	Greg Minney
4	10:20 – 10:35	MCPI/MSDR Update	Blaine Miner
5	10:35 – 10:50	Industry Test Focus Group Update	Tui Grant
6	10:50 – 11:20	Industry Go Live plan for May release and industry comms	Greg Minney/ Paul Lyttle
7	10:20 – 11:25	UFE Focus Group #5 - Update	Greg Minney
8	11:25 – 11:40	Industry Risk and Issues – March Review	Greg Minney
9	11:40 – 11:45	Forward Plan and Other Business - Tranche 2 rollout plans update	Greg Minney
10	11:45 – 11:50	Questions	Greg Minney
11	11:50 – 11:55	Meeting Close	Greg Minney

Actions

Greg Minney



Actions


ID	Status	Action	Comment
4.2.1	Complete	aseXML schema preference settings	AEMO has confirmed that by COB Friday 22 April 2022 participants will be requested to validate their aseXML schema preference settings as indicated in the Industry Go-live Plan.
4.8.2	Complete	AEMO to review assessment of risk R10.	Update included in Risk and Issues section of agenda
4.9.1	Open	Participants requested to provide updated tranche 2 metering rollout plans where applicable to GSMSTR@aemo.com.au , and to specify whether provided plans are to remain confidential to AEMO or are able to be shared to industry.	Rollout plan updates requested by 15 th March. 4 plan updates outstanding
4.9.2	Open	AEMO to circulate updated tranche 2 metering rollout plans where permission is given to do so.	Consolidated and individual plans to be circulated once all plans available

May 2022 Program Update

Greg Minney



May 2022 Release Timeline

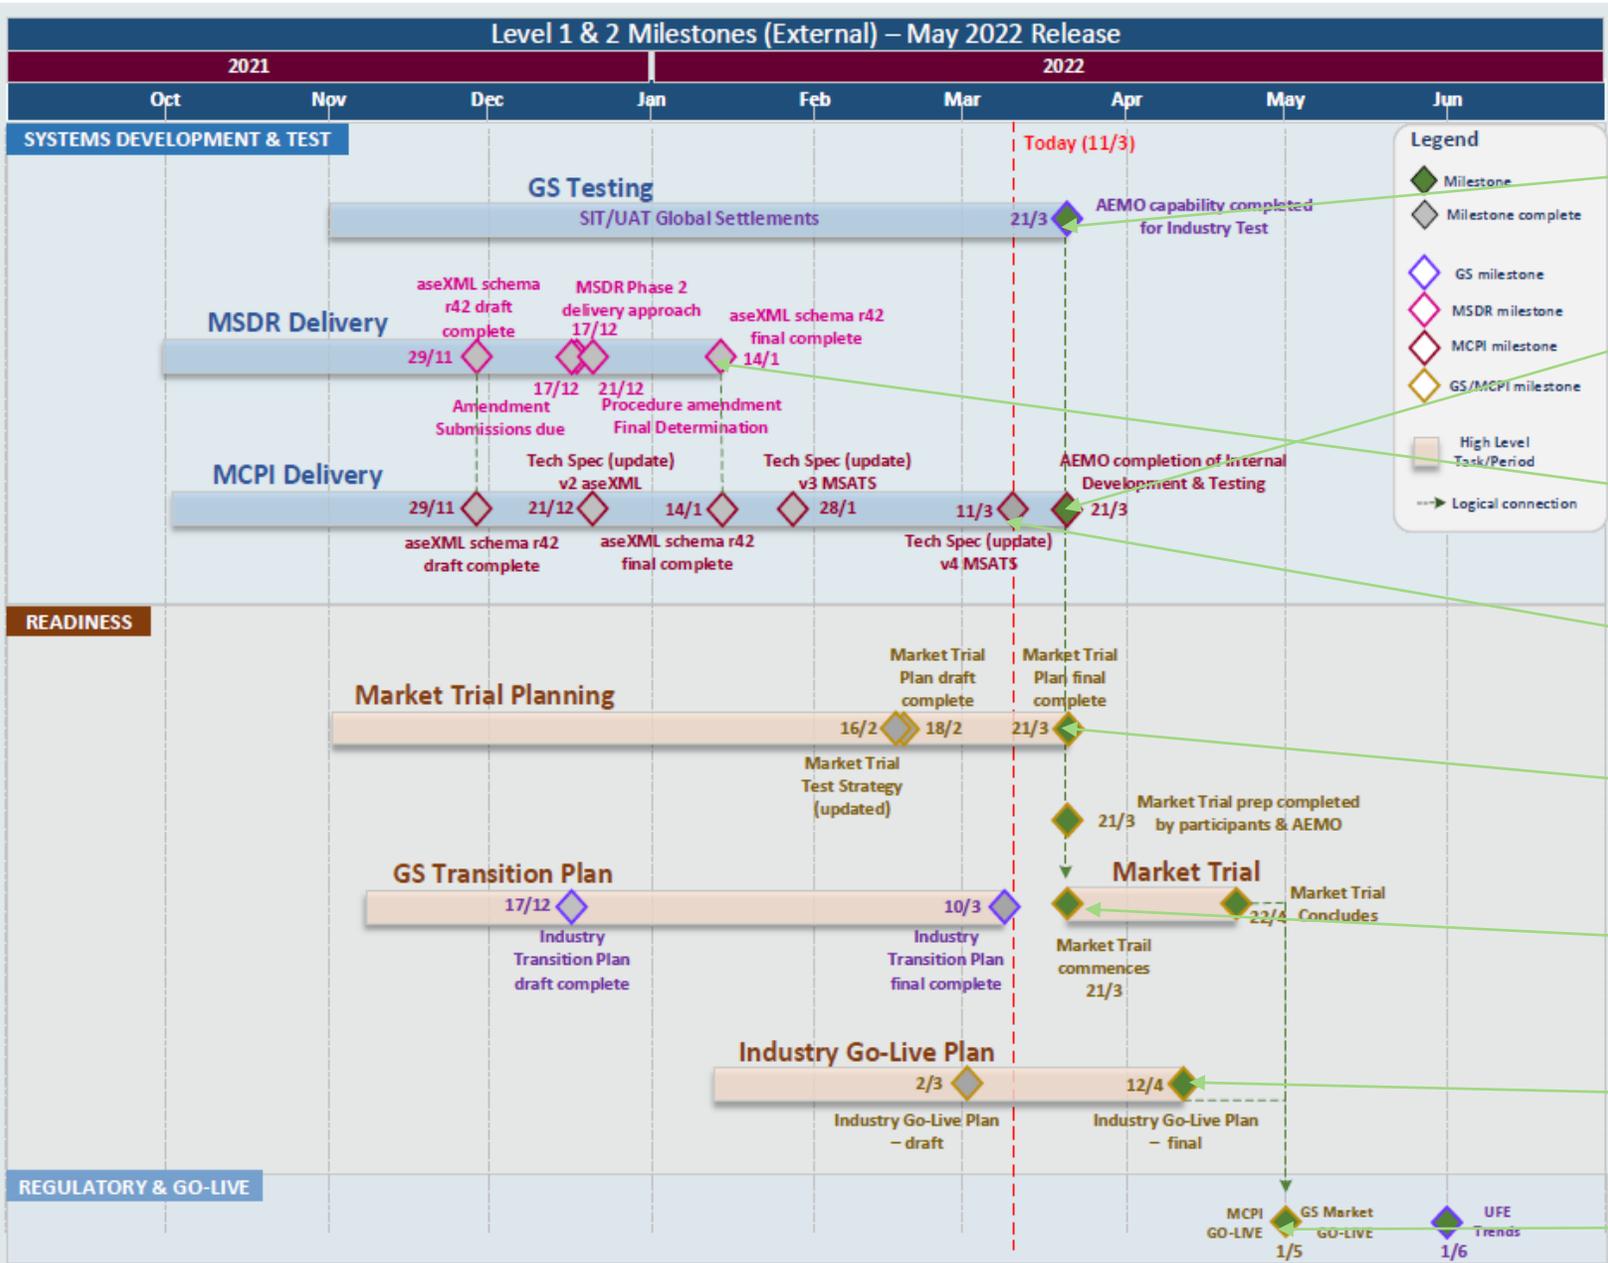

Some overlap of UAT completion and Market trial execution, with remaining tests performed during trial period

MCPI deployment included in 24th March code release, in line with industry testing requirements

MSDR delivery schedule to be confirmed via MSDR focus group

MCPI Tech Spec delivery v4 (47.2) delivered, including BUT specification

Market trial plan for GS settlement runs agreed based on backdating of LR responsibility

Market Trial commencement (Setup) from 21/3, Deployment 24th March, effective 27th March – On Track

Go-Live Approach drafted with GS Transition approach to be executed as part of Market Trial to finalise plans

MCPI and GS on track for Go-Live

May 2022 Milestone List (1/3)

ID	Description	Workstream	Date	Owner	Update
L2-MS/MC-01	Draft aseXML Schema r42 (includes MS DR and MCPI) presented to ASWG	MSDR / MCPI	29 Nov 21	AEMO	Complete
L2-MS-02	MSDR Procedure minor amendments process commences	MSDR	03-Dec-21	AEMO	Complete
L2-MS/MC-03	Final aseXML Schema r42	MSDR / MCPI	14-Jan-22	AEMO / ASWG	Complete
L2-RE40	Industry Transition Plan - GS (Draft update)	GS	17-Dec-21	AEMO	Complete
L2-MS09	MSDR Procedure minor amendments submissions due	MSDR	17-Dec-21	Participants	Complete
L2-MS05	MSDR Phase 2 delivery approach	MSDR	17-Dec-21	AEMO	Initial Draft released 17th December, updates to schedules communicated via MS DR focus group
L2-MC04	Tech Spec update v2 – MCPI CR Processing - aseXML edits	MCPI	21Dec-21	AEMO	Complete
L2-MC	Tech Spec update v3 – MCPI CR Processing - MSATS Config Changes	MCPI	31Jan -22	AEMO	Complete
L2- MC	Tech Spec update v4 – MCPI CR Processing - MSATS Code Changes	MCPI	28 Feb-22	AEMO	Complete
L2-RE37	May Release Industry Test Strategy	GS / MCPI	18 Feb 22	AEMO / Participants	Complete
L2-MS10	MSDR Procedure amendment Final Determination	MSDR	04-Feb-21	AEMO	Complete

May 2022 Milestone List (2/3)

ID	Description	Workstream	Date	Owner	Update
L2-MC06	User Guides Updates (GR processing)	MSDR	(TBC)	AEMO	Will not be issued for MCPI / May release, all changes incorporated into release for MSDR/ Nov
L2-RE38	Market Trial Plan - Draft	GS / MCPI	18-Feb-22	AEMO/ Participants	Complete – based on Market trial approach
L2-RE41	Industry Transition Plan -GS (Final)	GS	28-Feb-22	AEMO	complete
L2-RE42	AEMO capability completed for Market Trial / Industry Test	GS / MCPI	21-Mar-22	AEMO	On Track
TBC	MCPI/MSDR Data Transition Plan	MCPI/ MSDR	TBC	AEMO	As per MSDR Development Approach
L2-MC07	AEMO completion of Internal Development and testing	MCPI	21-Mar-22	AEMO	ON track for deployment 24 th March
L2-RE39	Market Trial Plan - Final	GS / MCPI	21-Mar-22	AEMO/ Participants	On Track- will address planned scenarios
L2-RE26/27	Market Trial Preparation completed	GS / MCPI	21-Mar-22	AEMO/ Participants	21 st March allows participant set up
L1-18	Market Trial Commencement	GS / MCPI	21-Mar-22	AEMO / Participants	Commence with "inflight" setup activities, cutover / GS Transition from 26th March
L2-RE21	May Release Go-Live Plan - Final	GS / MCPI	12-Apr-22	AEMO	On Track

May 2022 Milestone List (3/3)

ID	Description	Workstream	Date	Owner	Update
L1-20	Market Trial Completion	GS / MCPI	22-Apr-22	AEMO/ Participants	
L1-5	GS and MCPI Go Live	GS / MCPI	01-May-22	AEMO/ Participants	
L1-23	Trends in UFE Report	GS	01-Jun-22	AEMO	
L1-24	Guidelines for UFE Reporting Framework	GS	01-Mar- 23	AEMO	

MCPI/MSDR Update

Blaine Miner



MCPI/MSDR Update

- The third meeting of the MSDR Focus Group occurred on Tuesday 8 March
 - Discussion focused on determining the final data transition approach for MCPI/SIPF:
 - AEMO will defer its ‘transitional’ validations, relating to the SIPF field in CR5xxx transactions, until the end of the compliance holiday i.e. until 1 May 2023
 - LNSPs will initiate CR2xxx and CR5xxx transactions as required to accurately populate and maintain SIPF values from 1 May 2022
 - CR5xxx transactions to include any updates associated to verified shared fuse arrangements from 1 May 2022
 - LNSPs to use the Blind Update Tool (BUT) to perform mass updates to the SIPF field
 - AEMO is targeting the BUT to be available in Pre-prod by 23 May and Prod by 13 June
 - The BUT will be configured to:
 - Not allow the updating of an existing SIPF value in the MSATS database
 - Include BUT associated changes in the C1 reports
- MSATS Technical Specifications released Friday 11 March
 - Version 4.00 of the MSATS 47.1 Technical Specification (MSDR, MCPI, and GS)
 - Minor changes for the Blind Update tool only
 - Version 1.00 of the MSATS 47.2 Technical Specification (Blind Update Tool)
 - **This version is for information only. The design is not ready for participant builds.**
- The fourth meeting of the MSDR Focus Group occurred on Tuesday 22 March
 - Discussion focused on:
 - LNSPs SIPF standing data update plans
 - Initial consideration of MSDR data transition plan approach

Industry Test Focus Group Update

Tui Grant




May Release (GS and MCPI) Industry Go Live

Greg Minney and Paul Lyttle



High level Timeline

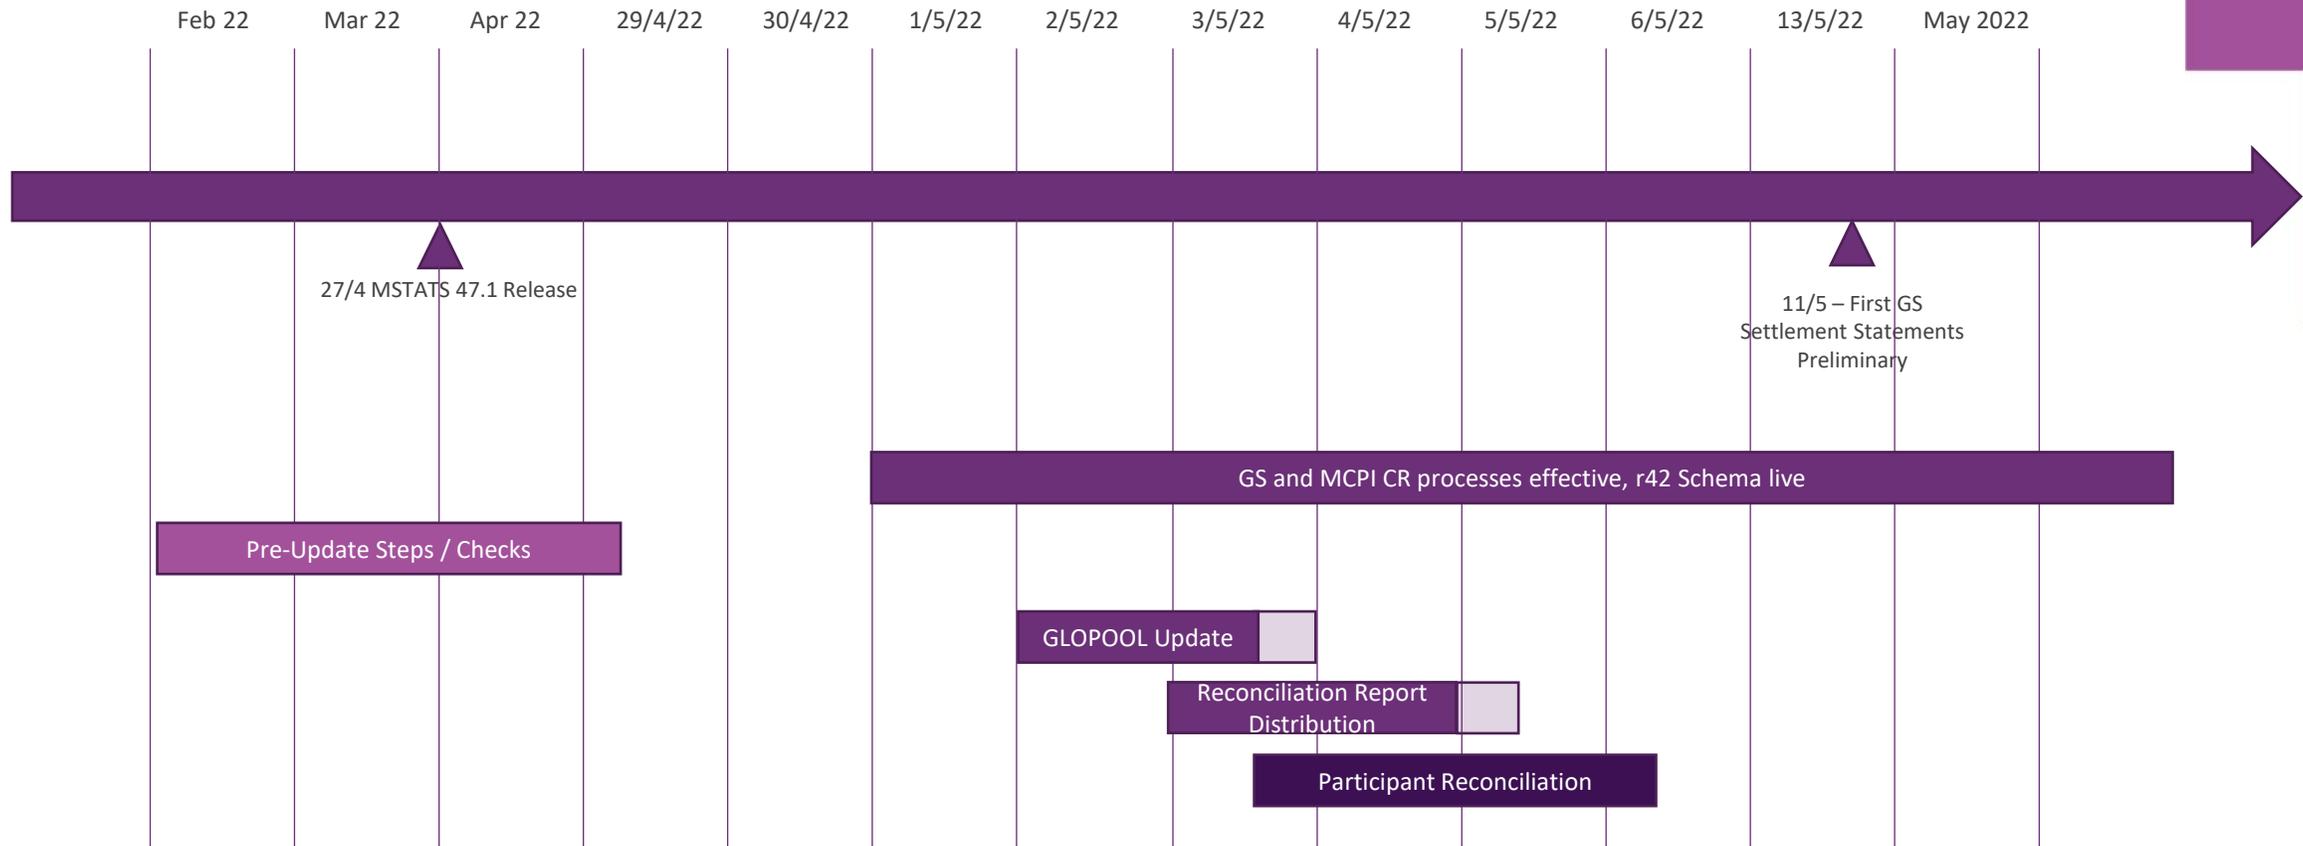

Industry Go-Live - Schedule

#	AEMO actions	Industry Impacts and actions	Planned Start Time (Market Time, Approximate only)	Communication Channel
1	Notice of planned release for MSATS 47.1 including r42 Schema		Wednesday 20 th April	Support Hub Bulletin
2		Participants confirm MSATS schema preferences in preparation for r42 schema release	Friday 22 nd April	GSMSDR Mailbox
3	AEMO provides extract <u>Count</u> of NMIs LR to be updated, and provide a <u>List</u> of NMIs FRMP to be updated		Tuesday 26 th April	List to be made available to LR participants only, Emailed to nominated account
4	AEMO deploys MSATS release 47.1 including r42 B2M schema	MSTATS, B2B and B2M outage during upgrade.	Wednesday 27 th 5.30 – 7.30 pm To be confirmed	Support Hub Bulletin at commencement and completion of outage?
5	MSATS 47.1 deployed	R42 Schema live, B2M schema preferences activated MSATS , B2B and B2M available	Wednesday 27 th April 7.30pm	Support Hub Bulletin on outage completion
6	AEMO notifies Participants to stop raising NMI Create prior to GS update run	Participant to hold NMI create from 11:59 pm 29 th April - until completion of Bulk Gloopool update – Task 12	Friday 29 th April 10:00 am	GSMSDR Mailbox

Industry Go-Live - Schedule

#	AEMO actions	Industry Impacts and actions	Planned Start Time (Market Time, Approximate only)	Communication Channel
7	GS and MCPI procedure changes become effective	CR 200x, 505X transaction apply validation validations for changes effective post 1/5	Sunday 1 st May 12.01 AM	Nil
8	AEMO commences “GLOPOOL” Update	No MSATS outage. NMI discovery may return GLOPOOL or previous LR value during update period. No standing data replication to eMDM until completion of all updates	Monday 2 nd May 3:00 am	GSMSDR Mailbox
9	AEMO Provides progress update on BCT updates – includes estimate of completion progress		Monday 2 nd May 9:00 am	GSMSDR Mailbox
10	AEMO Provides progress update on BCT updates – includes estimate of completion progress		Monday 2 nd May 3:00 pm	GSMSDR Mailbox
11	AEMO Provides progress update on BCT updates – includes estimate of completion progress		Monday 2 nd May 9:00 pm	GSMSDR Mailbox
12	AEMO Provides progress update on BCT updates confirm Completion of BCT / MSATS update and will commence eMDM Standing Data Update	All GLOPOOL updates applied to MSATS Participants can recommence NMI create activity	Monday 2 nd May 11:30 pm	GSMSDR Mailbox

Industry Go-Live - Schedule

#	AEMO actions	Industry Impacts and actions	Planned Start Time (Market Time, Approximate only)	Communication Channel
13	AEMO notifies participants that Metering data ingestion will be paused during Standing Data Synchronisation		Tuesday 3 rd May 4:00am	GSMSDR Mailbox
14	AEMO pauses Meter Data Ingestion during eMDM standing data synchronisation	Metering Data will be accepted but not ingested. Delays in transaction acknowledgement, potential stop files, RW Settlement report requests not processed (see note)	Tuesday 3 rd May 6:00am	
15	AEMO restarts Meter Data Ingestion	Backlog files will commence reprocessing. RM Settlement reports processed Standing Data synchronisation complete	Tuesday 3 rd May 9:00 am	GSMSDR Mailbox
16	AEMO finalises distribution of Reconciliation reports	Participant reconciliation of GLOPOOL updates	Thursday 5 th May 5.00pm	Email to participant registered address
17	AEMO produces first preliminary invoice (week 19) under Global Settlement regime	Commencement of financial settlement of UFE	Friday 14 th May	Settlement calendar
18	AEMO conducts Industry Q&A following production of preliminary statements for first Global Settlement run		Tuesday 17 th May 10:00	Invitation via UFE Focus Group

Feedback Summary

- Feedback received from 5 participants
- Updates / responses in progress and will be incorporated into revised plan.
- Follow up with participants where clarification is required
- Plan will be reissued post Preprod dry run to incorporate updated timings

Summary of feedback areas

Area	X-ref	Feedback / Clarification required
Time for Re-issue of Final Plan	Page 7	Potential to issue updated plan earlier than 12 April
Participant response to count of NMIs updated	Page 10 #3	Does AEMO expect participants to still validate and return the list of NMIs to AEMO by 28-Apr-22? If no feedback from participants is received, will AEMO still use the list that was originally sent?
Timing of software deployment	Page 10 #4	Can planned outage time be shifted later
NMI Creation	Page 10 #6	Clarify timing on hold of NMI creation and impact on in process NMIs including SIPP validation and clarification on create date versus effective date
Standing Data synchronisation	Page 10 #8	Clarification Impact of delay in standing Data synchronisation on meter data rejections
Metering Data ingestion	Page 11 #13	B2M or B2B meter data ingestion
Distribution of reconciliation reports	Page 12 # 16	Timing and participants who receive reconciliation reports
Timing of aseXML Schema update	13	Clarification on timing of participant schema updates
LR Updates at time of cutover	General	Clarification on activity in progress at time of cutover

UFE Focus Group Update

Greg Minney



UFE Focus Group Update

- 5th UFE Focus Group held 15 March
- Agenda
 - Progress on Areas since Go Live
 - Participant lead population activities – Status and impacts
- Discussion Topics
 - Review of UFE movements by profile area highlighting impacts of UFE building Blocks
- Next meeting scheduled for 13 April
 - RWG / UFE Focus Group members to forward key agenda items and confirm requirement for group to meet

Status of Global Settlement data updates

Below is a list of Participant related changes – Scheduled for UFE soft start 1/10/2021

- Create NMIs and activate datastreams, this includes:
 - Non Contestable Unmetered Loads – NCONUML
 - Completed with 101,169 Active NMIs
 - Tier 1 Basic NMIs and datastreams
 - Continuing with 49 NMIs still requiring update
 - Cross Boundary connection points – XBOUNDRY
 - Continuing with 90 Registered
 - Including 22 Greenfield, and
 - 12 still to be registered
- Standing Data Updates
 - Update Boundary loads from WHOLESAL to BULK
 - Completed with 1155 updated to BULK and 483 remaining as WHOLESAL
 - Update WHOLESAL NMIs connected to a distribution network to DWHOLSAL
 - AEMO continuing to investigate to ensure correct class code, currently 1 updated to DWHOLSAL
 - Update GENERATR NMIs to NREG where the FRMP Participant ID ends in “SGA”
 - Completed however Participants should continue to monitor, currently 1793 updated to NREG
- 5 Minute Meter Data
 - Update the Read Type Code all 5 minute capable meters to have a 4th character of ‘A’ or ‘D’
 - Deliver 5 Minute reads for all of the following connection types:
 - COMMS1, COMMS2 & COMMS3
 - 218 with incorrect RTC code.
 - COMMS4, COMMS4C & COMMS4D where the NMI Class Code is GENERATOR or NREG
 - 9 with incorrect RTC code.

Numbers provided as at 16 March 2022

All essential meters are providing 5 minute reads – monitoring continues

Industry Risks and Issues Review

Greg Minney


Updates on Risks / Issues



Approach to the risk review


- Review of trends and Risk ratings against key Industry risk and verification of mitigation strategies
- No new industry risks noted from previous review
- Risks raised relating to Nov 22 go-live will be managed through the MS DR FG to ensure that the RWG focuses on the May release

May 22 Readiness Risks



ID	Description	Inherent Rating	Controls/Comments	Residual Rating	Proposed Trend
R1	<p><u>Small participant readiness</u> Small participants are not adequately engaged due to resource limitations, resulting in small participants not having the ability or the information to execute their programs</p>	<p>Likelihood: Possible Consequence: Minor Rating: Medium</p>	<ul style="list-style-type: none"> AEMO completed a number of rounds of small participant mailouts Relevant FRMPs will have started to see UFE as a line item on their bill and should be aware of the changes Rule commencement does not require a critical mass of participant readiness (No Change) 	<p>Likelihood: Unlikely Consequence: Minor Rating: Low</p>	
R2	<p><u>Resources Constraints over summer period</u> There is a risk that there will be resource constraints over the summer period, particularly given the impact of covid and the intensity of 5MS, Customer Switching & WDR commencements. This could impact participant delivery plans for 1 May 2022</p>	<p>Likelihood: Possible Consequence: Moderate Rating: Significant</p>	<ul style="list-style-type: none"> Participants to manage their resource schedule and implementation plans Industry Test and Market Trials have been scheduled after the summer period where aligned resource delivery is required Scope of MSDR delivery removed from May release Propose this risk be closed 	<p>Likelihood: Unlikely Consequence: Moderate Rating: Medium</p>	
R3	<p><u>The AEMO business and operations are not ready for GS and MCPI on 1 May 22</u> The AEMO business may not be ready to deliver the full extent of the 5MS deliverables by 5MS and GS rule commencement including business processes and resource training, resulting in failure of Go Live for 5MS and GS Program</p>	<p>Likelihood: Possible Consequence: Major Rating: Significant</p>	<ul style="list-style-type: none"> L1 and L2 milestones have been established. Updated milestones pack is published monthly on the 5MS/GS webpages. GS rule commencement is incremental to 5MS implementations, Business resources are in place supporting current settlement processes with ongoing engagement approach established AEMO Delivery Program on track with testing underway and Market Trial to commence on schedule 	<p>Likelihood: Unlikely Consequence: Major Rating: Medium</p>	
R4	<p><u>Risk of AEMO cutover failure</u> There is a risk that AEMO systems will not go-live as scheduled with the planned cutover window resulting in an impact to participants' processes and market operations</p>	<p>Likelihood: Possible Consequence: Major Rating: Significant</p>	<ul style="list-style-type: none"> Cutover Planning including trial transitions to prove expected timings and manage impacts on production operations Transition approaches to be tested with industry during Market Trial Industry Go-Live Plans to be developed to establish production operation timings and review post execution 	<p>Likelihood: Unlikely Consequence: Major Rating: Medium</p>	
R5	<p><u>Resource constraints due to volume of market change</u> There is a risk that the key resources needed to focus on the upcoming rule changes are not able to do so due to these ongoing production defects as a result of recent changes including 5MS and re-platforming of AEMO systems.</p>	<p>Likelihood: Possible Consequence: Major Rating: Significant</p>	<ul style="list-style-type: none"> Participants to manage their resource schedule and implementation plans GS and MCPI go-live alignment to minimise overlapping change in 1st ½ of 2022 	TBC based on industry discussion	

May 22 Industry Risks



ID	Description	Inherent Rating	Controls/Comments	Residual Rating	
R6	<u>Insufficient time for industry development for r42</u> The industry consultation for r42 will push to beyond 10-Dec-21 and therefore into the end of year shutdown period. There is a (low) risk that the industry will not pick up the final r42 files in time for internal development and testing ahead of market trials	Likelihood: Unlikely Consequence: Minor Rating: Low	<ul style="list-style-type: none"> Functionality testing of new / changed fields beyond Shared Isolation Point Field not required prior November 7 release Data migration has been addressed in line with MSDR timeframes 	Likelihood: Unlikely Consequence: Minor Rating: Low	➔
R7	There is a risk that the schema cannot be sufficiently tested in May-22 as participants won't be ready to test all fields in the schema as/if a sufficient number of participants by role (FRMP, DNSP, MDP) is not ready to engage in testing. Specific focus needs to also be on 'negative testing', i.e. AEMO to not update fields even if provided	Likelihood: Unlikely Consequence: Minor Rating: Low	<ul style="list-style-type: none"> The only field to be communicated for May-22 is the Shared Isolation Point Field. Other changes will not be activated in B2M process prior to 7th November Changes for May available for Industry test from 24th March 	Likelihood: Unlikely Consequence: Minor Rating: Low	➔
R8	Late changes to the schema or procedural documents may result in rework and put regulatory timeline at risk	Likelihood: Unlikely Consequence: Moderate Rating: Medium	<ul style="list-style-type: none"> R42 schema has undergone extensive consultation through the ASWG and an open industry consultation. It is not expected that there will be additional changes post the final version being issued for the May release Procedure consultations took place in 2019 and a consolidation process is due for completion on 31-Jan-21 	Likelihood: Unlikely Consequence: Minor Rating: Low	➔
R9	Inconsistencies between schema and procedural documents may cause confusion, delays and rework and put regulatory timeline at risk	Likelihood: Unlikely Consequence: Minor Rating: Low	<ul style="list-style-type: none"> Risk for May is low as only changes is the Shared Isolation Point Flag Risk for November may be higher 	Likelihood: Unlikely Consequence: Minor Rating: Low	➔
R10	<u>BUT Production availability for participant use</u> Production availability of BUT update capability must provide for sufficient opportunity for participant testing prior to release to address potential impacts to participant operations and May 1 GS / MCPI delivery	Likelihood: Possible Consequence: Minor Rating Low	<ul style="list-style-type: none"> Proposed availability date for BUT / SIPF updates confirmed as post May 1 production release AEMO program to support Industry Test period, including issue resolution, prior to production release 	Likelihood: Possible Consequence: Minor Rating Low	⬇

Issues

ID	Description	Actions
I1	Schema update to r42 at same time as data update for Global Settlements role field from "LR" to "GLOPOOL" for all NMIs adds to risk of Go-Live activities	AEMO to understand the dependencies for participants. Both changes are required for MCPI and GS delivery Release and test process established with opportunity for Industry testing prior to go live Issue to be closed

Next Steps

- Industry Risks and Issues Register will be updated and published on the website
- Key risks will be reviewed on a monthly basis with new risks and issues being added as they arise
- Risks related to the Nov-22 go-live will be discussed through the MS DR FG
- RWG to provide any additional feedback on risks to GSMSDR@aemo.com.au

Forward Planning & Other Business

Greg Minney



Indicative RWG Topic Schedule

Month	RWG
November	<ul style="list-style-type: none"> ✓ Scope and governance confirmation ✓ Plan on a page/Milestone review ✓ Discuss key dependencies, risks and issues
December	<ul style="list-style-type: none"> ✓ Confirmation of key risks, issues and dependencies ✓ Test Strategy and trial approach ✓ Approach to GS Transition ✓ Progress updates
January	<ul style="list-style-type: none"> • Review milestone progress • Review GS Transition Plan • Tech Spec Approach (For MCPI) • Nov 22 Plan
February	<ul style="list-style-type: none"> • Review milestone progress, risks and issues • Market Trial Preparation • Industry Go-Live approach • Discuss key topics • Consider escalating items
March	<ul style="list-style-type: none"> • Review milestone and transition plan progress • Review risk and issues • Discuss the proposed Industry Go-Live Plan • Industry testing update
April	<ul style="list-style-type: none"> • Review milestone and transition plan progress • Receive Industry Testing Update • Finalise Industry Go-Live Plan
May	<p>Go Live Engagement approach for November release</p>

Other Business

- "Tranche 2" rollout plan updates and distribution
 - Requests for rollout plan updates extended with requested updates by 15th March
 - At issue of RWG pack 5 plan updates outstanding
 - Consolidated update will be provided once majority of updates have been received
 - Distribution will include those plans that have not been marked as confidential

Indicative Focus Group Topic Schedule

Month	Industry Testing FG	UFE FG	MSDR FG
November	N/A	✓ Complete	N/A
December	✓ Market Trial scope and timing	✓ Complete	N/A
January	<ul style="list-style-type: none"> Market Trial and Industry Test Approach 	<ul style="list-style-type: none"> Industry status on GS data population and provision Local Area Assessments Embedded Network treatment 	<ul style="list-style-type: none"> Scope and approach for MSDR FG
February	<ul style="list-style-type: none"> Develop Test Strategy/Plan 	<ul style="list-style-type: none"> Industry status on GS data population and provision Local Area Assessments Engagement approach 	<ul style="list-style-type: none"> TBC
March	<ul style="list-style-type: none"> Conduct participant testing 	<ul style="list-style-type: none"> Off market approaches 	<ul style="list-style-type: none"> TBC
April	<ul style="list-style-type: none"> Complete participant testing 		<ul style="list-style-type: none"> TBC

Upcoming Meetings



MARCH							APRIL							MAY						
Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa
		1	2	3	4	5						1	2	1	2	3	4	5	6	7
6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14
13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21
20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28
27	28	29	30	31			24	25	26	27	28	29	30	29	30	31				

WORKING GROUPS
Readiness (RWG)

FOCUS GROUPS
UFE (UFE FG)
Industry Testing (ITFG)
MSDR (MSDR FG)

OTHER
Q&A session
Industry Testing
National Public Holiday
State Public Holiday
AEMO Holiday Closure
*Relevant state has been marked in a comment for VIC, NSW, QLD & SA only.

Questions

